

ID	Task Name	Duration	Start	Finish	August						September			
					7/17	7/24	7/31	8/7	8/14	8/21	8/28	9/4	9/11	
1	Delayed Work	269 days	Tue 8/17/10	Fri 8/26/11										
2	Procure Louvers for Mech Rm	40 days	Thu 5/26/11	Wed 7/20/11										
3	IW / San Tie In Permits	256 days	Tue 8/17/10	Tue 8/9/11	Amtrak / CSX 									
4	Wheel Garden Pricing Revisions	23 days	Wed 6/22/11	Fri 7/22/11										
5	SWO & Release Demo of Runarounc	5 days	Wed 7/13/11	Tue 7/19/11	AK 									
6	Redesign Runaround track/pricing/N1	44 days	Tue 6/28/11	Fri 8/26/11	DBK/ AMTRAK 									
7	Site Related Work	80 days	Wed 6/1/11	Tue 9/20/11										
8	Sanitary IW Tie Ins	12 days	Wed 8/10/11	Thu 8/25/11	DERM / Redland 									
9	LOD Wheel Garden & Drainage Work	15 days	Tue 7/5/11	Mon 7/25/11	K 									
10	Wheel Garden Interior Bolts	4 days	Tue 7/26/11	Fri 7/29/11	Redland 									
11	Exterior Wheel Garden Slab	5 days	Tue 7/26/11	Mon 8/1/11	Redland 									
12	Demo Runaround Track	6 days	Thu 7/14/11	Thu 7/21/11	trac 									
13	Design & LOD North Track	40 days	Wed 6/1/11	Tue 7/26/11										
14	Materials North Track Mod	25 days	Wed 7/27/11	Tue 8/30/11										
15	Misc Switches & Turnouts	15 days	Wed 8/31/11	Tue 9/20/11	Amtrac 									
16	Track Ext North end to switch	8 days	Wed 8/31/11	Fri 9/9/11	Amtrac 									
17	Misc Switches & Turnouts	13 days	Tue 7/26/11	Thu 8/11/11	Amtrac 									

Project: Amtrak 7-15-11 Look Ahead.n Date: Thu 7/21/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	August						September			
					7/17	7/24	7/31	8/7	8/14	8/21	8/28	9/4	9/11	
18	Install water main	10 days	Tue 7/19/11	Mon 8/1/11	Redland									
19	Install exfiltration trench	10 days	Thu 7/28/11	Wed 8/10/11	Redland									
20	Rain leader storm tie ins	11 days	Mon 8/8/11	Mon 8/22/11	Redland									
21	Col Lines 1 - 17	4 days	Mon 7/25/11	Thu 7/28/11	Milestone									
22	Install Grating	4 days	Mon 7/25/11	Thu 7/28/11	Tiltcon									
23	Col Lines 17 - 32	25 days	Tue 7/5/11	Mon 8/8/11	External Task									
24	Lighting West side	8 days	Tue 7/5/11	Thu 7/14/11	External Task									
25	Overhead Cranes	7 days	Fri 7/29/11	Mon 8/8/11	MetCon									
26	Install grating	4 days	Mon 7/25/11	Thu 7/28/11	Tiltcon									
27	Col Lines 32 - 49	75 days	Mon 4/18/11	Thu 7/28/11	External Task									
28	Complete Railings	4 days	Mon 7/18/11	Thu 7/21/11	Whitley									
29	Install Grating	4 days	Mon 7/25/11	Thu 7/28/11	Tiltcon									
30	LOD Jib Crane	72 days	Mon 4/18/11	Mon 7/25/11	MTRAK									
31	Jib Crane Fdn	3 days	Tue 7/26/11	Thu 7/28/11	Tiltcon									
32	Mezzanine	18 days	Tue 7/5/11	Thu 7/28/11	External Task									
33	Mirrors	2 days	Tue 7/26/11	Wed 7/27/11	Champion									
34	Punch list prep - completion	18 days	Tue 7/5/11	Thu 7/28/11	External Task									

Project: Amtrak 7-15-11 Look Ahead.n Date: Thu 7/21/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	


ID	Task Name	Duration	Start	Finish	August						September			
					7/17	7/24	7/31	8/7	8/14	8/21	8/28	9/4	9/11	
35	General	95 days	Mon 4/18/11	Thu 8/25/11										
36	Track Int Wheel Garden	3 days	Tue 7/26/11	Thu 7/28/11										
37	Track Ext Wheel Garden	3 days	Tue 7/26/11	Thu 7/28/11										
38	LOD Mech Rm Louver	30 days	Wed 6/15/11	Tue 7/26/11										
39	Cut Louver opening install steel temp	4 days	Wed 7/27/11	Mon 8/1/11										
40	Relocate Air Tank	2 days	Wed 7/27/11	Thu 7/28/11										
41	Install Mech Rm Louver	4 days	Tue 8/16/11	Fri 8/19/11										
42	Complete Piping Mech Rm(Plbg)	4 days	Mon 8/22/11	Thu 8/25/11										
43	Complete Grout Pedestals North End	3 days	Mon 7/25/11	Wed 7/27/11										
44	LOD Modify Watering Cabinets	73 days	Mon 4/18/11	Tue 7/26/11										
45	H/U watering cabinets	10 days	Wed 7/27/11	Tue 8/9/11										
46	LOD Manipulator Changes	30 days	Wed 6/15/11	Tue 7/26/11										
47	Install Manipulators	3 days	Wed 7/27/11	Fri 7/29/11										
48	Install paint booth	6 days	Wed 7/13/11	Wed 7/20/11										
49	LOD FA Devices	15 days	Tue 7/5/11	Mon 7/25/11										
50	FA Strobes - Horns - Devices	5 days	Tue 7/26/11	Mon 8/1/11										
51	Conduit for Security System	13 days	Wed 7/6/11	Fri 7/22/11										

Project: Amtrak 7-15-11 Look Ahead.n Date: Thu 7/21/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	August						September			
					7/17	7/24	7/31	8/7	8/14	8/21	8/28	9/4	9/11	
52	Communications	25 days	Mon 6/27/11	Fri 7/29/11										
53	ADT Security For Amtrak	5 days	Mon 7/25/11	Fri 7/29/11										
54	At&T Tie In	5 days	Mon 8/1/11	Fri 8/5/11										
55	480V Utilities Relocation	195 days	Tue 1/4/11	Fri 9/30/11										
56	480V - Backfill Behind PMF	15 days	Fri 7/8/11	Thu 7/28/11										
57	480V - Stub ups & Brooks Boxes	15 days	Tue 7/12/11	Mon 8/1/11										
58	Jack & Bore - Electrician	2 days	Mon 7/25/11	Tue 7/26/11										
59	Equipment Commissioning	33 days	Wed 7/27/11	Fri 9/9/11										
60	Compressed Air System	2 days	Thu 7/28/11	Fri 7/29/11										
61	Manipulators	1 day	Tue 8/2/11	Tue 8/2/11										
62	Elevator	1 day	Tue 8/9/11	Tue 8/9/11										
63	Car Jacks	8 days	Tue 8/9/11	Thu 8/18/11										
64	Paint Booth	2 days	Wed 8/10/11	Thu 8/11/11										
65	Bridge Cranes	5 days	Mon 8/15/11	Fri 8/19/11										
66	Water Jet Cutter	2 days	Wed 8/17/11	Thu 8/18/11										
67	Carpet Extractor	1 day	Wed 8/17/11	Wed 8/17/11										
68	HVAC	1 day	Thu 8/18/11	Thu 8/18/11										

Project: Amtrak 7-15-11 Look Ahead.n Date: Thu 7/21/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	August							September			
					7/17	7/24	7/31	8/7	8/14	8/21	8/28	9/4	9/11		
69	Control Vending Equipment *	4 days	Mon 8/22/11	Thu 8/25/11											
70	Welding Booth	2 days	Tue 8/23/11	Wed 8/24/11											
71	Fire Alarm / Suppression System	1 day	Mon 8/29/11	Mon 8/29/11											
72	Sanitary Pumps - Lift Stations	2 days	Tue 8/30/11	Wed 8/31/11											
73	Generator	2 days	Wed 8/31/11	Thu 9/1/11											
74	Coach Watering Cabinets	2 days	Thu 9/1/11	Fri 9/2/11											
75	Parts Washer	2 days	Wed 9/7/11	Thu 9/8/11											
76	Truck Washer	3 days	Wed 9/7/11	Fri 9/9/11											
77	Derail System	2 days	Wed 9/7/11	Thu 9/8/11											
78	IT Kiosk	1 day	Wed 9/7/11	Wed 9/7/11											
79	Wayside Power Cabinets	1 day	Thu 9/8/11	Thu 9/8/11											
80	Toilet Dumps	1 day	Thu 9/8/11	Thu 9/8/11											
81	Motorized Curtain	1 day	Fri 9/9/11	Fri 9/9/11											
82	Jib Crane	1 day	Fri 9/9/11	Fri 9/9/11											
83	Dishwasher	1 day	Fri 9/9/11	Fri 9/9/11											
84	Facility Training Sessions	10 days	Mon 9/12/11	Fri 9/23/11											

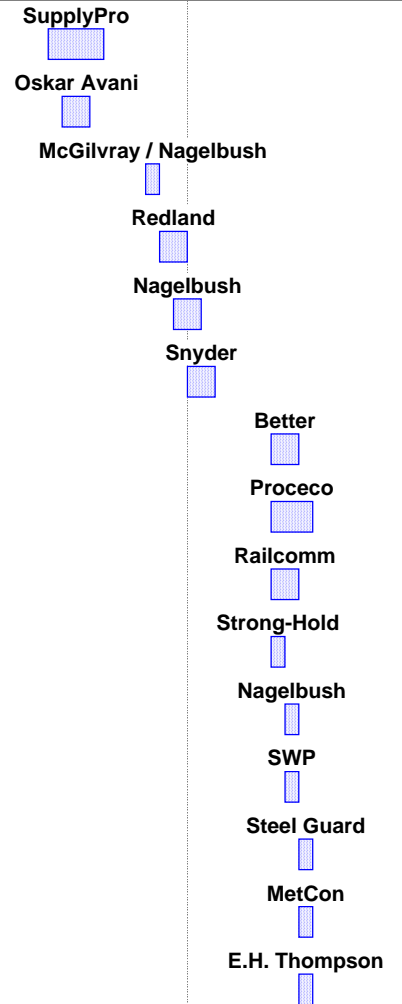

Project: Amtrak 7-15-11 Look Ahead.n Date: Thu 7/21/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
